


**CIHA Projects and Maintenance Operations and Storage Facility
Construction Progress Report
November 2017**



Installation of cabinets in utility area.



Exterior and roll up doors installed on rentals.

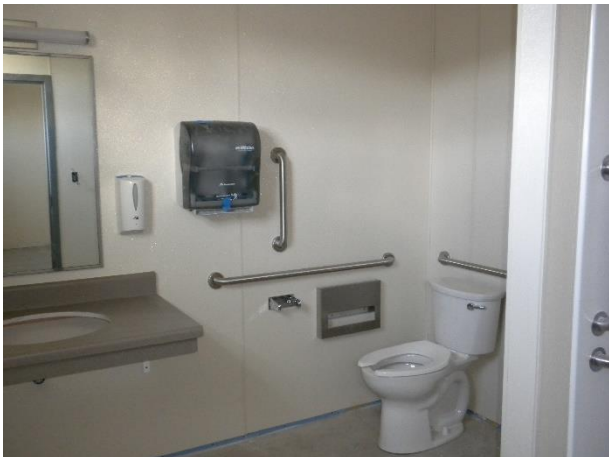

Installation of bathroom finishes complete.

Work Summary

Completed
November 2017

- Electrical finishes completed.
- Interior grid ceiling installed.
- Bathroom finishes completed.
- Interior doors installed.
- Cabinets installed.
- Metal siding completed.
- Painting completed.

Anticipated
December 2017

- Installation of water tanks.
- Final punch list.
- Scheduling fencing installation.

**CIHA Projects and Maintenance Operations and Storage Facility
Construction Progress Report
November 2017**



Security cameras at entries to rentals.



Pouring a pad for the water tanks.



Overhead view of CIHA shop from Tribal shop.

Cost Summary

Original Contract Amount	\$1,771,188
Changes to Contract	43,915
Current Contract Amount	1,815,103
Previous Billed Amount	1,558,165
Previous Balance Remaining	256,938
Current Payment Due	243,022
Remaining Balance	\$ 13,916
Billing Percentage This Month	13%
Total Billing Percentage to Date	99%

Change Orders

Approved:

- Change Order No. 4 adding threshold and water dam to ADA emergency shower, exterior recessed light for fire riser room, concrete for water tanks, and crushed gravel to improve parking areas. Contract addition \$19,491.

Potential/Upcoming:

- None.

Project Issues

- Damage to roll up doors and problems with track installation.
